

SHIFT STATUS REPORT

Overall Status



Current Status



Project

Waitrose Balham

Location

Balham

Date

26/08/2026

Overall Status & Key Activities:

-  Shopfloor decoration
-  T&J
-  Cold-room build
-  Roof works
-  External decoration
-  FRV coldroom latex

Planned Works:

-  As per Programme Rev F issued.
-  Roof works continued
-  Service counter hand over
-  Internal decorations
-  Internal signage
-  Checkpoint visit
-  Matwell

Overview:

Roof delays – Programme with set dates to be issued.

Status Report

Project Waitrose Balham

Location Balham

Overall Status




Current Status




Brief	Status	Comments
Programme		Revision F issued – Constant review/amendments.
Partner Routes		All routes to be left clear of combustible materials and obstacles ; as per site Fire Plan
H&S		Ongoing review on working areas & safety paperwork. Near miss noted by Waitrose (actioned)
Housekeeping		All welfare facilities to be respected. Continuous monitoring by UCB
Emergency Procedures		All emergency procedures are in place
Accidents/ Near Miss		0 accident. H&S Visit due Tuesday 07/06/26 to review incident report. 1 near miss cable pulling debris.
AOB		

Lux Levels

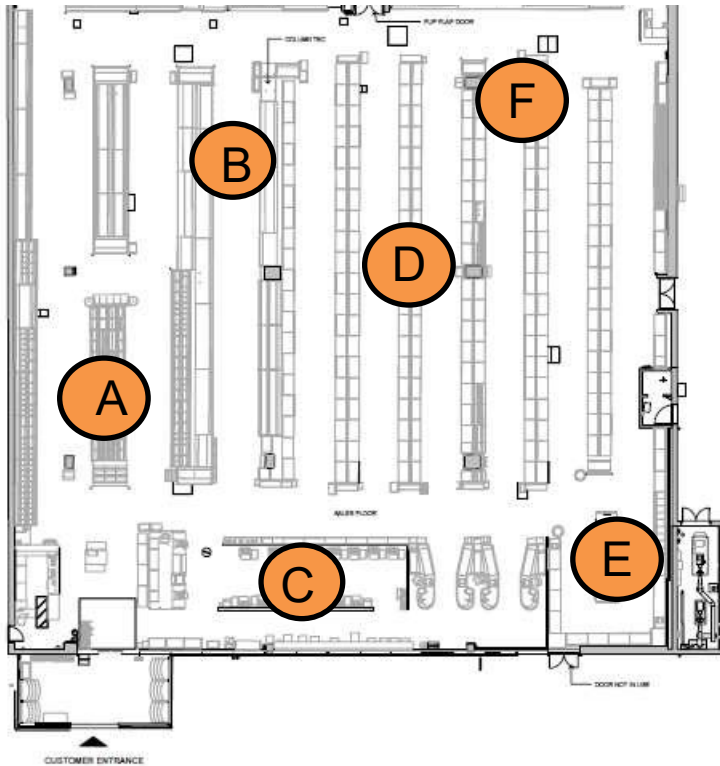


Area	Level Prior to Works Commencing	Current Level
A - FRV	500	550
B – Chilled	530	600
C – Checkouts	650	700
D – Ambient	520	690
E – BWS	446	530
F – Shop floor General	560	680

Back of House Temperature Readings

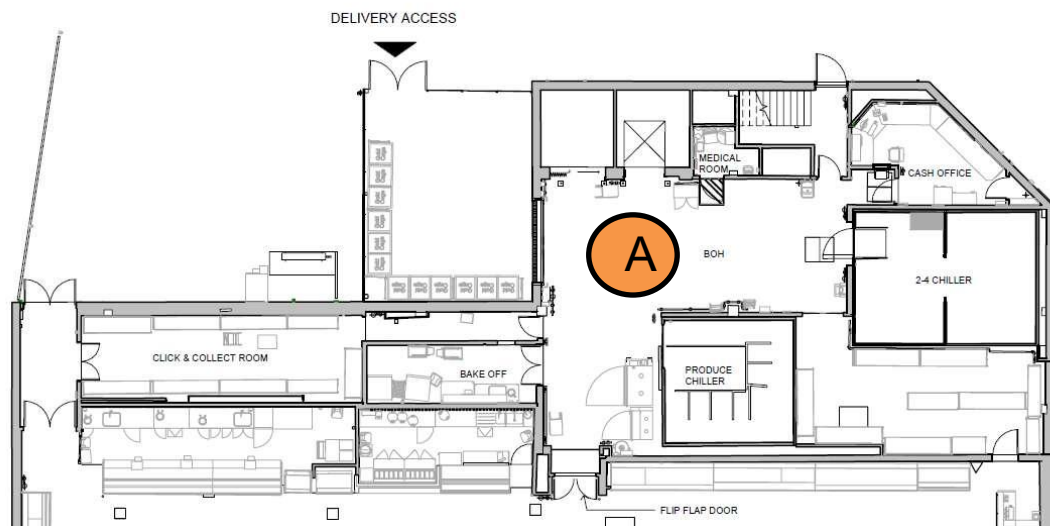

Area	Temperature Readings
A - BOH	18

Sales Floor Temperature Readings

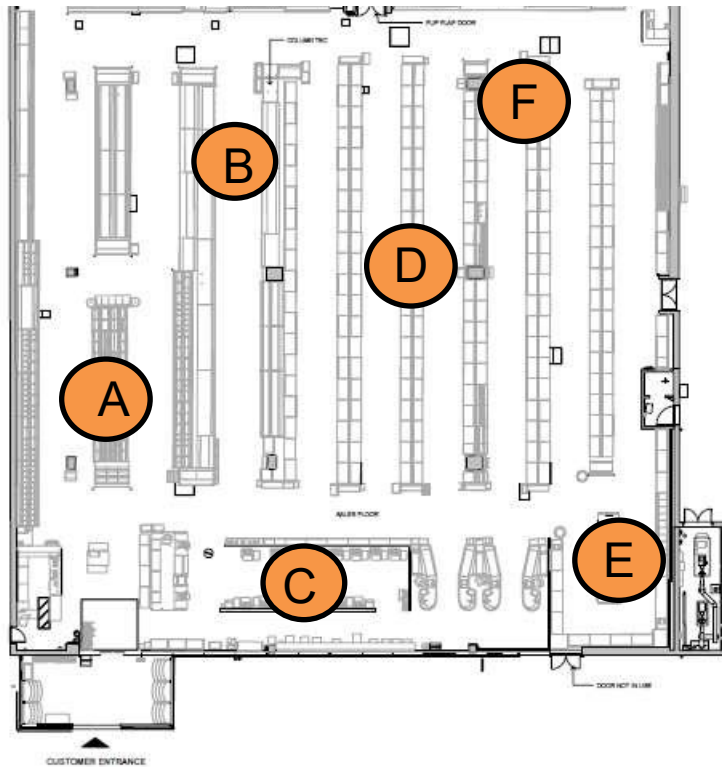

Area	Temperature Readings
A - FRV	19
B – Chilled	19
C – Checkouts	19
D – Ambient	18.7
E – BWS	19.1
F – Shop floor General	19.1

Progress Photos



External decoration

Progress Photos



External decoration

Progress Photos




Floor cleaning

Progress Photos



Floor cleaning

Progress Photos

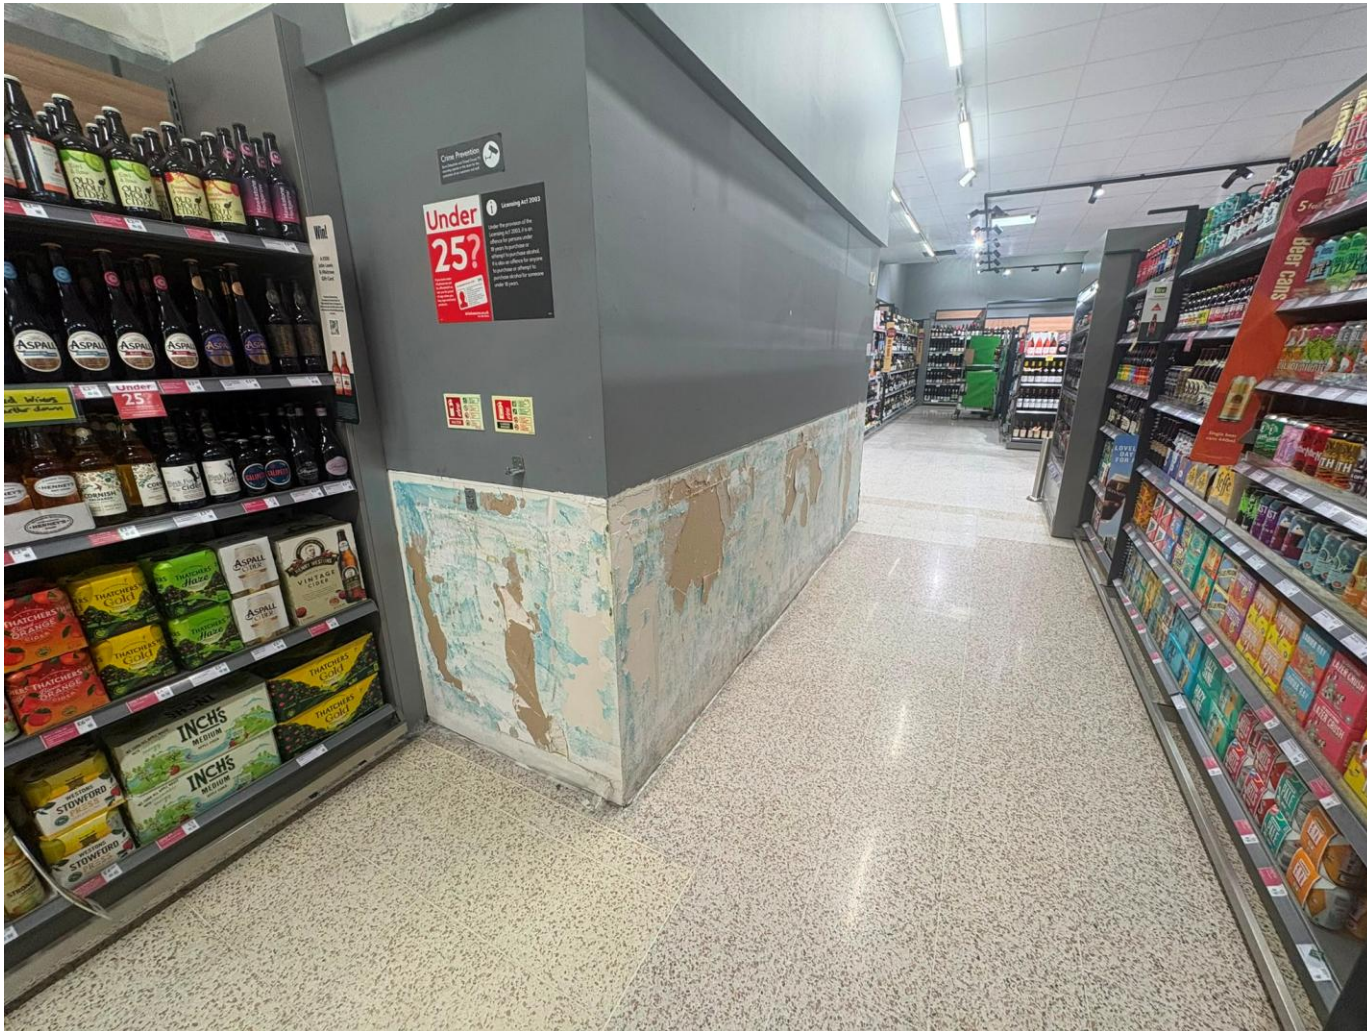

Removal of laminate

Progress Photos



Service drop decoration

Progress Photos



PDR carpet

Progress Photos



Cigarette kiosk wall decoration

Progress Photos



FRV cold-room self level


Progress Photos



Racking BOH

Signing in Sheet Night Shift


SIGNING IN REGISTER
HS-CON-RG-04
Version 04 – February 2026



Project: Balham

Date	Name	Company	Time	
			In	Out
26/8	Aidan	uc build	7:30	out
	D. Wicks	MSB	7:45	12:30
	HPHARRIS	CA FIC	7:55	
	Jeddy Du Preez	OPUS	8:00	
	Antonio Maximo	OPUS	8:00	
26/8	Ion Lincoln	PINC	8:28	
26/8	M. BONNEL	MSB	8:00	16:00
26/8	M. Galt	UCB	16:45	
26/8	L. Gbelle	UCB	2:00	3:00
26/8	S. Fortescue	UCB	2:00	3:00
26/8	Billy	UCB	2:00	3:00
26/8	S. Philp	UCB	2:00	3:00
26/8	D. Kelly	UCB	2:00	3:00
26/8	Ryan Chalky	UCB	2:00	3:00
26/8	DAN CLARKE	NLA	2:00	03:30
26/8	DANIEL	UCB	2:15	06:20
26/8	P. ALI	PROLINE	21:00	04:10
26/8	George C	WOODWARD	21:00	04:00
26/8	Laurentiu N	WOODWARD	21:00	04:00
26/8	Tucker. J	Freemaster	22:00	5:00
26/8	Jed. 2	Freemaster	22:00	7:00

SIGNING IN REGISTER
HS-CON-RG-04
Version 04 – February 2026



Project: Balham

Balham.

Date	Name	Company	Time	
			In	Out
26/8	R. RYAN + GARGIE	SMER	2:30	03:30
26/8	STEFANIA	PINC	21:40	06:10
26/8	CONSTANTIN	PINC	21:40	06:10
26/8	Albert Korkun	JME	2:50	03:30
27/8	Aidan	uc build	7:30	
27/8	Antonio Maximo	OPUS	7:40	
27/8	BUGDIT M. C	UNION	2:50	

Daily Fire Safety Checklist

This checklist to be completed by Branch Management Team AND the Main Contractor
Carried out at least 2 times a day - start of the contractor's shift and end of the contractor's shift

Route 1: SHOP, Route 2: BOH, Route 3: STAIRS, Branch: BATHAM, Date: 26/27 Aug 2026

Item	Description	Yes	No	Action
All Inspections				
1.	Fire escape routes throughout store clean and clear - inside and outside - and emergency lighting operational	☒	☐	
2.	Fire escape routes through construction site clean and clear - inside and outside - and emergency lighting operational	☒	☐	
3.	All Store fire safety signage fully operational	☒	☐	
4.	All fire doors throughout store fully operational	☒	☐	ROOF DOOR WORKS CHECKING G
5.	Work area temporary and emergency lighting fully operational (if it is an escape route)	☒	☐	
6.	Work area emergency exit signs in place and fully operational	☒	☐	
7.	Smoke ventilation systems fully operational	☒	☐	
8.	Combustible construction materials removed or protected	☒	☐	
9.	Penetrations formed through fire walls or ceilings as a result of construction works are appropriately sealed	☒	☐	X TBA -
10.	Hot Works Permits (HWP's) in operation	☒	☐	N/A NOT ISSUED
Start of Shift				
11.	All FFE in place. Partners informed of changes.	☒	☐	
12.	Fire alarm installation working but with appropriate heat / smoke detectors in work area bagged/covered or isolated	☒	☐	FEEDBACK WORKING ON ALARM TUNING
13.	Sprinkler System isolated / deactivated (if applicable)	☒	☐	X OFF
14.	HWP's - work areas inspected before issue	☒	☐	N/A NOT ISSUED
15.	Changes to escape routes. Partners informed of changes.	☒	☐	
16.	Is there any information arising from this inspection or changes to fire arrangements that needs to be conveyed to contractors	☒	☐	MC to action
17.	Is there any information arising from this inspection or changes to fire arrangements that needs to be conveyed to Partners	☒	☐	BM to action
End of Shift				
18.	Fire alarm installation working but with appropriate heat / smoke detectors in work area bagged/covered	☒	☐	
19.	Sprinkler System re-activated (if applicable)	☒	☐	OFF
20.	HWP's - work areas inspected to close permits	☒	☐	N/A NONE ISSUED

Time 06:15 Signed MC R. Mayre Signed BM A. R.

Please Retain all documents for File

Client Handover Sheet

John Lewis Partnership

Fire Safety Checklist – Handover of Sales Areas to Branch

Branch: Batham (N)

Item	Description	RACI	Confirmed to Standard	Further Action
1.	All Fire Alarm call points in place and operational	MC/PM	☒	
2.	Fire alarm system in place and fully operational	MC/PM	☒	STILL UNDER MAINTENANCE
3.	Smoke heads/heat detectors debugged and operational	MC/PM	☒	NOT TOUCHED
4.	All FFE in place and operational	MC/PM	☒	
5.	All Fire signage in place and operational (inside and outside)	MC/PM	☒	
6.	All emergency lighting in place and operational (inside and outside)	MC/PM	☒	
7.	Fire escape doors operational	MC/PM	☒	ROOF DOOR WORKS WORK
8.	Fire escape routes clear of debris (inside and outside)	MC/PM	☒	
9.	Sprinkler system in place and operational	MC/PM	☒	OFF
10.	Penetrations sealed by FIRAS accredited fire stopping company	MC	☒	TBA
11.	Magnetic locking devices all fully operational and Partners inducted on their use / over-ride system	MC/PM	☒	
12.	All electrical certificates received	MC/PM	☒	
13.	Fire Alarm certificates received	MC/PM	☒	
14.	Sprinkler system certificates received	MC/PM	☒	AVE & WIND TEST
15.	Branch Fire Risk Assessment reviewed and updated	MoM / BMT	☒	
16.	Branch Emergency Procedures reviewed and updated	BM/PM	☒	
17.	Branch Fire Log reviewed and updated	BM/PM	☒	

New area cannot be handed over until all items verified as being complete and in place.

Signed Main Contractor (MC) R. Mayre

Signed Branch Management Team (BMT) A. R.

Signed Project Manager (PM)

Date: 26/27 Aug 2026

Please Retain all Documents for File

Call and Response Tracker

[illegible]
