

CA Drillers Ltd

Unit 2, CA Business Park, Colewood Road
Whitstable, CT5 2RP

Telephone: 01227 458883

Website <https://www.cadrillers.com>



RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)

Reference: CAD/UR/W/ MAS/CN - 3647

Revision Number: 1

Author: Calvin Nash

Job Role: SHEQ Manager

Date Created: 26 Aug 26

Date Modified: 26 Aug 26

1.0 Method Statement

- | | |
|--|--|
| 1.1 - Scope of works | 1.2 - Training & Competence |
| 1.3 - Personnel involved in this project | 1.4 - Access arrangements |
| 1.5 - Tools and equipment | 1.6 - Special permits |
| 1.7 - PPE requirements | 1.8 - Specific PPE requirements |
| 1.9 - Manual handling | 1.10 - Legislation |
| 1.11 - Waste Management | 1.12 - Welfare provision |
| 1.13 - First aid provision | 1.14 - Emergency procedures |
| 1.15 - Near Miss Reporting | 1.16 - Location of Nearest A&E |
| 1.17 - Amendments and Authorisation | 1.18 - Risk Assessment and Method Statement Sign Off |

2.0 Sequence of Works

- 2.1 Diamond Drilling and Sawing
 - 2.1.1 - General
 - 2.1.2 - Diamond Drilling
 - 2.1.3 - Handheld Drilling Dry and Wet

3.0 Risk Assessment

- | | |
|--|---------------------------------|
| 3.1 - Hidden live services | 3.2 - Live electrical services |
| 3.3 - Hand Tools (Use of) | 3.4 - Noise |
| 3.5 - Out of hours working | 3.6 - Working on external sites |
| 3.7 - Dusty environment, including silica dust | 3.8 - Manual Handling |

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)

Reference: CAD/UR/W/ MAS/CN - 3647

Page: 1 of 41

Date updated: 26 Aug 26

- 3.9 - Power tools (Including hand held power tools)
- 3.11 - Vibrating tools and equipment
- 3.13 - Cables
- 3.15 - Stairs
- 3.17 - Ground level obstacles
- 3.10 - Rotating cutting equipment
- 3.12 - Work from MEWPS, cherry pickers, scissor lift or other mechanical height access equipment
- 3.14 - Slippery substances
- 3.16 - Materials stored at ground level
- 3.18 - Ground conditions (Terrain)

4.0 COSHH Assessment

4.1 - Silica Dust

CA Drillers Ltd

Unit 2, CA Business Park, Colewood Road
Whitstable, CT5 2RP

Telephone: 01227 458883

Website <https://www.cadrillers.com>



1.0 Method Statement

**Project: RAMS - Uplands Retail Ltd -
Waitrose - Newport (Corre Holes)**

Reference: CAD/UR/W/ MAS/CN - 3647

Site Address:

Waitrose

Audley Road

Newport

TF10 7DS

Client: Uplands Retail Ltd

Start date: 28 Aug 26

End/Review date: 28 Oct 26

Works Supervisor: Matty Singlehurst (Uplands Site
Manager)

Works Supervisor phone: 07880 359 311

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)

Reference: CAD/UR/W/ MAS/CN - 3647

Page: 3 of 41

Date updated: 28 Aug 26

1.1 Scope of works

HOLD POINT - PRIOR TO ANY WORKS COMMENCING PLEASE ENSURE ALL WORK LOCATIONS HAVE BEEN SCANNED FOR HIDDEN LIVE SERVICES BY THE CLIENT, AS THIS IS THEIR RESPONSIBILITY UNLESS NOTIFIED AND AGREED OTHERWISE

CAD Scope of Works at Waitrose, Newport for Uplands Retail -

Works for Out of Hours Working on Friday 28th August 20.00pm to 22.00pm

- CAD to undertake core drilling at high level at Waitrose within the rear service yard.
- Uplands to ensure all live services have been isolated or / and fully protected with these being clearly identified to the CAD operatives.
- Works are deemed as W.A.H with Uplands providing access in the form of a certified MEWP for CAD to use. Any permits required for W.A.H to be issued by Uplands and briefed to CAD prior to commencement
- Uplands to clearly mark out hole positions on the external brick wall
- Core Holes to be drilled as follows through external brick and internal block wall -

2no x 152mm diameter

2no x 107mm diameter

1no x 76mm diameter

- CAD to use dust suppression when drilling at all times
- Works are out of hours and must be carried out between 20.00pm to 22.00pm
- Full access to the working area is to be provided to CAD



Hole Positions - Waitrose, Newport

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Core Holes)

Reference: CAD/UR/W/ MAS/CN - 3847

Page: 4 of 41

Date updated: 26 Aug 26

1.2 Training & Competence

CA Drillers has competent and sufficiently trained operatives to carry out the tasks required as part of a project, the following professional qualifications and certifications are typically expected depending on the nature and scope of works.

- Diamond Drilling and Sawing NVQ 2 & 3 Skilled Worker
- SMSTS
- SSSTS
- CSCS
- IPAF
- Manual Handling
- Abrasive Wheels
- Asbestos Awareness
- PASMA

1.3 Personnel involved in this project

CAD Operatives - TBC

CAD Contacts List -	
Position :	Name:
Main office/Emergency:	Head Office - 01227 458883
Contracts Director:	Craig Murphy - 07508 452287
Operations Manager:	Steve Dunk - 07515 018397
Senior SHEQ Manager:	Ian Purdie - 07949941087
SHEQ Manager	Calvin Nash - 07943 712745
Contract Managers:	Chris Massat- 07496 398621
	Gary Jarvis - 07947 405520
	Koisha Kayn - 07463 621178
	Graham Field - 07956 586031
Gareth Towers - 0092 101864	
CAD Operatives	TBC

CA Drillers Contact Details

1.4 Access arrangements

All company operatives and sub-contractors will be inducted in before commencing with work on site.

Access and egress from the site shall be via the designated entrance and exit routes provided by the Principal Contractor. The Site Manager or Delegate will be informed of any problems with access & egress routes should they arise.

Upon arrival, all company operatives and sub-contractors will sign in at the Site office (Or other designated area) before accessing the working area on site. Before leaving the site, all company operatives and Sub-contractors will sign out.

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Hoies)

Reference: CAD/UR/W/ MAS/CN - 3647

Page: 5 of 41

Date updated: 26 Aug 26

1.5 Tools and equipment

All tools and equipment utilised throughout the project shall be in good working order and inspected according to any relevant statutory provisions explicitly placed upon the tool or equipment. The Accompanying risk assessment shall identify the control measures that all employees and contractors shall adhere to safely operate company (including hired) tools and equipment while on site.

If any tool or item of equipment is found to be impaired or not suitable for the task for any reason, it shall be removed from service and a suitable alternative sourced.

**3-Speed Diamond Core Drill
DK 17 Wet + Dry**



Copyright © 2004 by John Wiley & Sons, Inc.


Technical Data		
Type		DN 11
Material group	58	20.04
Overall length	mm	734.0
Overall spread	1 mm	540.120/200.0
Length	mm	470
Weight	kg	0.4
Flange Ø outside		
DN 11 (DN 10 connection)	mm	55.120
Flange Ø inside	mm	47.120
Flange Ø inside - Ø outside	mm	27.000
Flange thickness	mm	5.500/4.000
Max. design temp. of medium	mm	65
Max. design temp. of medium		8.7.15

Thompson
Laura Drake

WEKA

Chen et al.

DK 17 Handheld

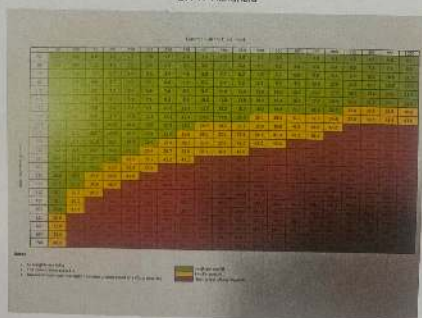

bare weight

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)

Reference: CAD/UR/W/ MAS/CN - 3647

Page: 6 of 41

Date updated: 26 Aug 26

1.6 Special permits

Any permits required to facilitate the works are to be provided by Uplands to CAD

1.7 PPE requirements



Respiratory
Protection



Ear Protection
(Bs en 352)



Eye Protection
Safety Goggles
(Bs en 166)



Protective
Gloves



Protective
Footwear with
Mid Sole
Protection (BS
EN ISO 20346)



Head protection
(En 397)



Hi Visibility
Clothing (Bs en
471)

1.8 Specific PPE requirements

All standard PPE required for site work shall be provided and used at all times by the Company's Staff and Contractors.

Standard PPE

While on site, all staff shall be required to wear the above PPE at all times.

Task-Specific PPE

Details of all specific PPE requirements required out-with the standard identified above is within any accompanying COSHH assessment or specific risk assessments contained within this document.

- Ear Defenders
- FFP 3 Respiratory Equipment -

All operatives required to wear FFP3 Respiratory Protective Equipment (RPE) must hold a valid Face Fit Testing Certificate. Face fit testing ensures that the FFP3 mask forms an effective seal around the wearer's face, providing the required level of protection against airborne contaminants such as silica dust, concrete dust, fumes, and other hazardous particulates that may be present during CA Drillers' activities.


In accordance with HSE guidance (HSG53), an FFP3 mask cannot provide adequate protection if the wearer:

- Fails a face fit test
- Has facial hair that prevents an effective seal (including stubble, moustaches, beards, or any unshaven areas that interfere with mask fit)
- Is unable to achieve a reliable seal due to face shape, scarring, or other medical/physical factors


1.9 Manual handling

Where possible, all equipment and materials shall be transported using mechanical means.

Where equipment and materials are to be lifted and carried, all company operatives shall adopt Kinetic lifting methods as depicted below:

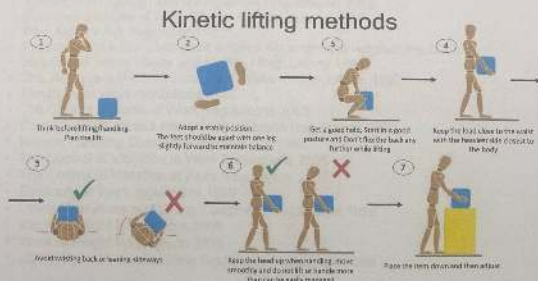

Kinetic Lifting techniques

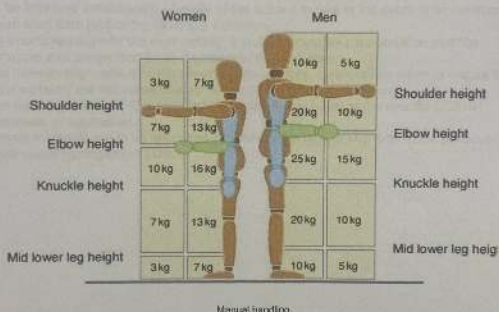

1.10 Legislation

Associated legislation:

- Health and Safety at Work Act 1974.
- Environmental Protection Act 1990.
- Reporting of Injuries, Diseases and Dangerous Occurrence Regulations 2013.
- Construction (Design and Management Regulations) 2015.
- Provision and Use of Work Equipment Regulations 1998.
- First Aid at Work Regulations 1981.
- Personal Protective Equipment at Work (Amendment) Regulations 2022.
- Health and Safety (Signs and Signals) Regulations 1996.
- The Workplace (Health, Safety and Welfare) Regulations 1992.
- Electricity at Work regulations 1989
- The Control of Noise at Work Regulations 2005
- Control of Substances Hazardous to Health Regulations 2002
- Manual Handling Operations Regulations 1992
- The Control of Vibration at Work Regulations 2005
- The Control of Vibration at Work Regulations 2005
- Electricity at Work regulations 1989
- Lifting Operations and Lifting Equipment Regulations 1998
- Work at Height Regulations 2005
- Work at Height Regulations 2005
- Lifting Operations and Lifting Equipment Regulations 1998

1.11 Waste Management

In the event of any environmental incidents, including spillages, the Site Manager or Delegate must be informed immediately – Details of the actions to take in the event of an environmental incident shall form part of the initial site induction.

Before commencing with the work activity, a suitable route for transportation must be determined and understood by all members of the work party.

When transporting waste through internal thoroughfares, care shall be taken to ensure that interior surfaces are not contaminated or damaged by waste materials.

When handling waste, PPE is required according to site rules, or the specific COSHH assessment (if applicable).

All waste materials are to be deposited into the correct type of skip &/or waste bin according to the site waste management plan.

1.12 Welfare provision

Provision of welfare arrangements on site is the responsibility of the Principal Contractor.

All welfare facilities shall be compliant with Schedule 2 of the Construction (Design & Management) regulations - this includes the provision, as a minimum, of the following:

- Toilets (Including female facilities where required),
- Washing facilities,
- Clean, wholesome drinking water,
- A suitable supply of cups, drinking vessels or a water fountain,
- Arrangements for the provision of boiled water,
- Changing rooms and lockers,
- Heating,
- Rest facilities,
- Drying facilities.

All welfare facilities on site are required to be safe and hygienic.

1.13 First aid provision

All Operatives shall refer to the onsite safety notice board for all first aid information; All operatives will be shown the location of the safety notice board during the site induction.

The quantity of site first aid boxes shall be proportionate to the number of Operatives and site and stocked with contents according to BS 8599 unless a site first aid assessment dictates otherwise

The Principal Contractor shall be responsible for the site first aid provisions.

The quantity of Site first aiders shall be according to the First aid at work Approved Code of Practice document L74; details are in the table below:

Type of Industry	How many persons employed	Number of trained and competent first aiders required
	Less than 25	At least 1 appointed first aider
<u>Low hazard</u> - Offices, shops, libraries etc.	Between 25 and 50	At least 1 Emergency first aid at work trained first aiders
	More than 50	At least 1 first aid at work trained first aider for every 100 persons employed
	Less than 5	At least 1 appointed first aider
<u>Higher hazard</u> - Light engineering and assembly work, food processing, warehousing, extensive work with dangerous machinery or heavy instruments, construction, chemical manufacture etc.	Between 5 and 50	At least 1 Emergency first aid at work trained first aiders depending on the type of injury which may occur.
	More than 50	At least 1 first aid at work trained first aider for every 50 persons employed

First aiders on site guidance (Quantity)

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)
Reference: CAD/UR/W/ MAS/CN - 3647

Page: 11 of 41
Date updated: 26 Aug 26

1.14 Emergency procedures

Development and implementation of site emergency procedures is the responsibility of the Principal Contractor. Details of site emergency procedures are within the Construction phase plan.

Instruction and information related to site emergency procedures will take place during the site induction which all personnel are required to attend. In the event of uncertainty, all site operatives should discuss with the Site Manager or Health and safety support.

If any of the site emergency procedures change, all Operatives shall be informed to ensure that they are aware of all emergency requirements at all times.

1.15 Near Miss Reporting

Please scan this QR code to report any events or dangerous occurrences that did not cause harm but had the potential to cause injury or ill health



By reporting a near miss they can be acted on and safety measures put into place to prevent harm in the workplace in the future

Please scan this QR code to report any events or dangerous occurrences that did not cause harm but had the potential to cause injury or ill health

1.16 Location of Nearest A&E

Princess Royal Hospital

Apley Castle, Telford, TF1 6TF

Tel - 01952 641222

1.17 Amendments and Authorisation

In the event of changes from the proposed work scope, that job will be stopped and re-assessed.

The Works Supervisor will notify the Company Director (or delegate) and Site Manager and inform them of the change to the workscope.

If required, the RAMs document will be edited as necessary to reflect a significant change and re-submitted to the Site Manager or Delegate for approval.

1.18 Risk Assessment and Method Statement Sign Off

Risk Assessment and Method Statement Sign Off

To be signed off by a competent person:

Name of Competent Person: Calvin Nash

Position: SHEQ Manager

Date: 26.08.2026

Signature:

Calvin Nash

2.0 Sequence of Works

2.1 Diamond Drilling and Sawing

2.1.1 General

- Attend client site induction.
- Induction to cover site procedures for working during COVID-19 and Construction Leadership Council (CLC) procedures v7.
- SSSTS and CSCS operatives have read and signed the method statement for works being undertaken and attended the daily safe start briefing and toolbox talks.
- All persons are shown the access / egress routes daily during the Safe Start briefings to notify of planned works.
- Obtain any permits from client if required.
- SSSTS to check all sawing works have been marked out by client.
- SSSTS to check all drilling works have been marked out by client.
- All operatives to wear correct PPE and RPE.
- Set up core control / slurry / water measures.
- Set up equipment, power and water.
- Start drilling operations.
- Complete operations.
- Stockpile debris for client to remove and replace during work.
- Leave all areas clean, safe and tidy.
- Ask client to check completed works and move onto next area.

2.1.2 Diamond Drilling

- The diamond drilling equipment will be delivered to site via the correct designated site entrance and then on to the work area.
- Exclusion zones will be set up around our work areas. All dust / core and slurry control measures will be implemented to all the areas with acro and board propping to prevent any cores from falling.

- All holes to be pilot drilled if requested.
- Water hoses to be run out from mains water supply provided by site and power leads from main power supply. Both hoses and leads will be fixed off the floor where possible so they are not a trip hazard.
- Operatives will only drill marked out holes by client. Podiums to be used for any drilling work above 2.5m in height.
- Following the equipment instruction manual, the drilling rig will be secured to the wall with drop in anchors where the drill motor and drill bit will line up with the marked hole. The trigger time use for percussion drilling will not exceed levels that may cause hand arm vibration issues as the time will be approximately 30 seconds per fixing.
- Once all equipment is fixed and secured and all areas are safe drilling shall commence.
- The correct diameter core will be drilled then removed to site skips.

2.1.3 Handheld Drilling Dry and Wet

- C A Drillers operatives move all drilling equipment to the works location. The 110v handheld drilling equipment will be delivered to site via the correct designated site entrance, pre work check will be carried out on the machine to look for any malfunctions and ensure it is in good working order before work commences.
- Operatives connect the handheld drill to the H class filter dust collector LEV vacuum, this is used to encapsulate dust produced by the core drilling, furthermore, operatives run out 110v power leads to connect the handheld drill for the core holes through the slab,
- Alternatively, if the LEV is not suitable for the task at hand, operatives will core using water to assist in drilling and eliminating the dust pollution. Operatives run out water hoses from the mains situ on site, this is used to cool and lubricate the drill bit in motion while mitigating the production of dust when drilling.
- Operative lines the drill bit up with the core marking, this will be drilled freehand and the operative will ensure it is held as vertical/horizontal as possible, applying pressure to the hand-held drill until the depth required is obtained. Operatives must operate the handheld drill with both hands to ensure full control over the drill at all times, operatives must not come into close proximity when the drill bit is in full spin drilling motion.
- The drill bit is lowered and introduced to the surface slowly to mitigate kick back, the operative will slowly apply enough pressure to core the hole but be sure not too apply too much pressure, this is to eliminate the drill bit snagging.
- As each hole is completed the core is removed, the drill will then be repositioned to the next location and repeated until all required holes have been drilled. The core/ drill bit is then de cored and cleared to the skip provided. Once all works have been completed all equipment will be cleared from the work area and operatives to remove the debris to the correct waste stream skips provided. The respective work areas are left in a tidy, safe and respectable manner

3.0 Risk Assessment

Risk Matrix

The hazards and associated risks with this activity have been identified and given a scored rating using semi-quantitative risk assessment methodology.

The risk assessment ratings are a subjective estimate based on the knowledge of the assessor and identify the level of risk without controls and also the level of residual risk once the control measures have been implemented.

To calculate risk rating, and residual risk rating you should multiply the Likelihood (1-5) by the Potential severity of injury (1-5) as depicted below.

Likelihood of injury	4	Low risk	This level of risk is acceptable to the company. Proceed with caution and stop the job if anything changes.
	x		
Severity of injury	5	Medium risk	This level of risk is acceptable to the company if it cannot be reduced further following a review by an Authorised Person within the company.
	=		
Risk/Residual risk	20	High risk	This level of risk is unacceptable and additional controls are needed to reduce the overall level of risk to an acceptable level.

Severity of injury	Likelihood of injury				
	1 Remote	2 Unlikely	3 Possible	4 Probable	5 Certain
Negligible injury such as bruises and abrasions	1	2	3	4	5
Minor injury requiring first aid treatment	2	4	6	8	10
1-7 day absence from work injury	3	6	9	12	15
Regulatory reportable injury, disease or event	4	8	12	16	20
Disability, fatality or injury to the public	5	10	15	20	25

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)
Reference: CAD/URW/ MAS/ CN - 3647

Page: 16 of 41
Date updated: 26 Aug 26

3.1 Hidden live services

Hazard Description: 3.1.1 Surface with potential hidden live cables

Person at risk: Operative performing the work

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All live electrics identified and warning notices fitted where live electrics cannot be made dead during work.	1
• Explosion	x		x
• Electrocution	5	All Operatives will review and understand the emergency response plan before starting work.	5
• Loss of services	=		=
	20	All work is planned and supervised by a competent Person to reduce the likelihood of damage and disruption to services.	5

Before work within floors or ceiling areas, the persons completing the work shall check to ensure that are no services hidden within any work area.

Ensure all workers are aware of any live circuits through inductions and regular toolbox talks before starting work.

Live wire detector used on the surface and review the up-to-date service drawings before drilling or breaking into the wall.

No works to be carried out directly on live equipment - Stop the job if unknown cables are identified during the works.

Prevent direct contact by ensuring all insulation barriers/covers are fitted to any electrical boards, equipment etc. by a trained and competent electrician.

Works to control access of Site operatives into areas of risk, employing a permit to work system if there is any risk of contact with live electricity is present.

3.2 Live electrical services

Hazard Description: 3.2.1 Hidden or Live electrical services near to work area
Person at risk: Operative performing the work, Other Site Operatives, Public

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	5		1
• Electrocution	x	A competent person is nominated to supervise the task.	x
• Serious Injury	5		5
• Burns	=	So far as is reasonably practicable PHYSICAL PROOF OF DISCONNECTION SHALL BE OBTAINED.	=
• Loss of power and services	25		5

All services shall be treated as being live until all services have been proven to be isolated by responsible contractor/ principal contractor.

In the event that the above is not possible a survey shall be carried out by a competent person using appropriate survey tools and equipment, i.e. Cat and Genny - any services identified will be marked. The C A Drillers and the client will be notified if any services are in the path of the proposed works and works will be suspended until alternative arrangements have been made with the client and no services are in the path of proposed works.

In the event that this is found not to be reasonably practicable, works will stop in accordance to identified risk, a on point risk assessment will be conducted with information being fed back to all relevant managers (C A Drillers and Client). A safe system of work shall be developed, identifying the hazards that are likely to be encountered during the work by making a suitable and sufficient task specific assessment of the risks posed by those hazards. Clear information on the type, location and status of services, the tools, equipment and working practices that will be required to avoid damaging the services shall be provided.

The location of any uncharted services discovered shall be recorded and marked on site using the most appropriate method.

Any exposed services that have the potential to come in contact with works (falling materials, water ingress, striking...) shall be isolated and protected

accordingly (ie: services trays shall be protected using plywood covers) by the client unless requested to do so by the client.

All activities which involve working in close proximity to live services shall be controlled under a permit to work system or under a SSOW which has been agreed upon by both C A Drillers and the client.

In the event that it is essential to continue working in an area where live services have been discovered, so far as is reasonably practicable, arrangements shall be made for the services to be made dead.

In the event that this is found not to be reasonably practicable, a safe system of work shall be developed, identifying the hazards that are likely to be encountered during the work by making a suitable and sufficient task specific assessment of the risks posed by those hazards. Clear information on the type, location and status of services, the tools, equipment and working practices that will be required to avoid damaging the services shall be provided.

Exposed services shall be protected from vibration, the elements, falling materials and ingress of water by use of suitable means.

In case of a service strike, the Client and CA Driller Supervisor/manager will be notified immediately and if safe, the area is to be segregated against unauthorised access. Works will stop until written confirmation that the area is made safe is obtained from all parties involved.

In the event of a service strike the immediate area shall be evacuated of all personnel, all managers from the relevant parties will be informed.

All electrical systems to be completely isolated wherever practicable, by a competent Electrician.

Competent Electrician and Site Supervisor will identify any live circuits and fit warning notices accordingly to the live circuits that cannot be isolated during the work activity.

Ensure all workers are aware of any live circuits before commencing with the activity.

Inform all operatives of any live electrical services and how to avoid injury before starting work.

Warning signs compliant with the Health and Safety (Signs and signals) regulations displayed on all live equipment.

Further Guidance

HSG47 - Avoiding Danger From Underground Services.

3.3 Hand Tools (Use of)

Hazard Description: 3.3.1 Hand tools

Person at risk: Operative performing the work

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	Do not use modified tools.	1
• Personal injury including	x	Inspect all hand tools prior to use to ensure that they are in good condition.	x
• Bruising	3		3
• Cuts	=	Keep all hand tools in tool bags/boxes when not in use.	=
• Eye damage	12	Operatives must be deemed competent to use relevant hand tools.	3
		Return all defective tools and equipment to the Line Supervisor and quarantine.	
		Use all tools and equipment in the manner in which they were designed to be used.	
		Wear Level 5 cut resistant gloves when using sharp/bladed tools.	

3.4 Noise

Hazard Description: 3.4.1 Operation and use of tools, equipment and machinery which emit loud noise over a short period of time

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	A selection of hearing protection is available for the user including ear plugs and ear defenders as required.	1
• Hearing damage	x		x
• Headaches	4	All audible warning sounds have sufficient volume and frequency to alert all Operatives working within the area of any potential danger.	4
• Stress	=		=
	16	All operatives have been provided with information, instruction and training around working in noisy environments or operating noisy plant and equipment.	4
		All Operatives within the area must wear protection provided when operating or using noisy tools, equipment or machinery.	
		Always use hearing protection when using power tools.	
		Exposure to noise will not exceed 87 dB (a) for weekly personal noise exposure or 140 dB (a) for peak sound pressure.	
		Hearing protection provided shall not reduce the ambient noise levels to below 70 dB (a).	
		Noise risk assessment to be undertaken by a competent person to identify durations that Operatives can work within designated high noise areas.	
		Persons within areas where power tools are being used to wear hearing protection.	

3.5 Out of hours working

Hazard Description: 3.5.1 Weekend & Out of Hours Working

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of sudden medical crisis	3	Operatives to be supervised during the works	5
	x	No lone working over the weekends or out of hours working	x
Risk of accident / injury without having the ability to communicate to others on site	4	CAD operatives to be briefed again on emergency procedures for the weekend and OOH working	1
	=		=
Delayed rescue or first aid administration	12	CAD supervisor to be provided with site contact details for Uplands Site Manager	5
Lack of communication with other site workers if they are off at the weekends			

Hazard Description: 3.5.2 Work Outside of General Working Hours

Person at risk: Operative performing the work

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	Mobile phone or 2-way communication device provided to Operative/s in case of emergencies.	1
• Accident or incident without the ability to communicate to others	x		x
	3	Out of hours work procedure to be explained to all Operatives during the Company/Site Induction.	3
	=		=
	12	Site security informed of Operatives working out of hours on site.	3
		The Principal Contractor will determine the type of work that is allowed out of hours and any restrictions on work activities.	

3.6 Working on external sites

Hazard Description: 3.6.1 Company Operative working on external site
Person at risk: Operative performing the work

Risk	Risk Rating	Control measures	Residual Risk
Increased risk of injury due to:	4	A full induction provided to all Operatives by the site Duty holder before starting work on site.	1
• The employee being unfamiliar with the orientation of the site	x		x
• Lack of knowledge of actions to take in an emergency	3	Erect barriers with appropriate signage around the Work area.	3
• Health and hygiene-related issues	=		=
	12	Hand tools and power tools will not be left unattended.	3
		Operative to become familiar with the site fire safety and emergency response arrangements on site before commencing with work activity.	
		Operative to inform all personnel who may be affected by the works of the hazards and associated risks.	
		The site will be made safe at the end of each shift.	
		Welfare facilities available for all site Operatives, per the workplace (health, safety and welfare) regulations &/or Construction (Design and Management) regulations (where applicable).	

Hazard Description: 3.6.2 Access to and from site including parking of vehicles
Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	3	A Banksman will control all Reversing vehicles at all times if reversing is unavoidable	1
• Collision with vehicle	x		x
• Fatality	5	All Operatives to abide by site traffic management plan.	5
• Serious injury	=		=
	15	All Operatives will sign in before entry on site.	5
		All Operatives will sign out before leaving the Site.	
		Alternative access provided for pedestrians which segregates them from the ongoing work.	

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)
Reference: CAD/UR/M/ MAS/CN - 3647

Page: 23 of 41
Date updated: 26 Aug 26

3.7 Dusty environment, including silica dust

Hazard Description: 3.7.1 Construction Dust

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	So far as is reasonably practicable work methods which limit the production of dust shall be implemented.	1
• Lung cancer	x		x
• Silicosis	5	All cutting of materials shall be undertaken in a specific location as instructed by the Site Manager and following CIS36 and INDG463.	5
• Chronic Obstructive Pulmonary Disorder	=		=
• Occupational asthma	20	So far as is reasonably practicable dust shall be kept below the Workplace Exposure Limit (WEL) of 0.1 mg/m ³ over a Time Weighted Average (TWA) of 8 hours.	5
		All Operatives face-fit tested by a competent person before wearing respiratory protective equipment.	
		Water sourced to the floor saw will be used as a wet cutting method to mitigate exposure to airborne dust.	
		Water suppression used when alternative methods of suppression are not suitable.	
		Wear any additional Personal Protective Equipment (PPE) identified within the COSHH assessment as required.	
		Wear any additional Respiratory Protective Equipment (RPE) identified within the COSHH assessment as required.	
		Where possible, Operatives will use a less powerful tool that creates less dust.	
		Waste materials shall be removed on a regular basis to prevent dust-spread.	
		High dust & slurry producing activities i.e. floor saw cutting or demolition, shall be limited during periods of high wind.	

3.8 Manual Handling

Hazard Description: 3.8.1 Manual transport of equipment or materials
Person at risk: Operative performing the work

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All staff have trained in kinetic manual handling techniques.	1
• Musculoskeletal disorders	x		x
• Work-related upper limb disorders	3	Assess the best way to lift before moving the load, with the heaviest part of the load close to the trunk of the body.	3
• Sprains and strains	=		=
• Dropped objects	12	Before transporting manually transporting any equipment or materials, ensure that the route to be taken is clear of any obstructions. Remove any potential hazards before carrying the material where possible.	3
• Slips, trips and falls			

Manual handling risk assessment to be developed for the activity and understood by all members of the work party.

Manually handle all materials on a firm and level ground where possible.

Operatives shall wear gloves to increase adhesion when manually transferring loads.

Operatives will not lift beyond their capabilities and will seek help for any load they consider too heavy or hazardous to lift.

Team lift any loads that exceed the maximum guidance weight of 25kg.

When bending and crouching, bend from your knees, not your back.

When handling hot, cold or sharp items ensure correct gloves are worn.

Where possible, mechanical lifting aids will be used to deliver and position heavy equipment and materials.

Where possible, the load will be separated into smaller parts and increasing the frequency of the route rather than the overall weight being carried at any one time.

3.9 Power tools (including hand held power tools)

Hazard Description: 3.9.1 Use of power tools, including hand held power tools
Person at risk: Operative performing the work

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	A visual inspection must be carried out before use, any defects must be reported and the equipment withdrawn from service for repair or replacement as required.	1
• Cutting	x		x
• Stabbing	5		5
• Penetrating Wounds	=	All personnel wearing respiratory protective equipment shall be Face fit tested by a competent person.	=
• Entanglement with tool bits	20		5
• Lacerations			
• Eye damage			
• Hearing damage			
		All power tools and machinery must be regularly inspected and maintained in good condition.	
		Allow time for equipment to stop before placing into storage.	
		Always use hearing protection when using power tools.	
		Area to be segregated using barriers with appropriate warning signage to prevent unauthorised access into the work area.	
		Battery operated tools considered before the use of low voltage tools and equipment.	
		Goggles manufactured to the relevant British standard (BS EN 166) worn while operating power tools.	
		Only trained and experienced operatives are allowed to use Power tools, inexperienced or young workers are kept under strict supervision while using power tools.	
		Operatives prohibited from wearing loose clothing or gloves or use rags or other materials which could become entangled with moving parts.	
		Operatives to wear suitable protective gloves to prevent friction burns and good grip when adjusting the position.	

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)

Reference: CAD/UR/W/ MAS/CN - 3647

Page: 26 of 41

Date updated: 26 Aug 26

3.10 Rotating cutting equipment

Hazard Description: 3.10.1 Using Drilling and Sawing tools

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
• Lacerations	3	<i>All operatives to hold NVQ Level 2 or 3 in</i>	1
• Entrapment	x	<i>Diamond Drilling and Sawing</i>	x
• Drawing in	5	Core Drilling	5
• Trapped Fingers	=		=
	15	Pre visual checks prior to starting work.	5
		No loose clothing, jewellery and long hair tied back.	
		Correct PPE to be worn when handling/operating the drilling equipment.	
		Sufficient water to be used to prevent over heating of the drill and drill bit, this which creates a jam up in the core hole and also wear and tear to consumables.	
		Moving concrete cores to a safe area.	
		Operatives use a wet vacuum hoover to suction water and slurry created by the core drilling.	
		Slurry to be disposed of correctly in correspondence with the sites COSHH waste management.	

3.11 Vibrating tools and equipment

Hazard Description: 3.11.1 Use of vibrating tools and equipment
Person at risk: Operative performing the work

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	The task shall be planned accordingly, with the SSOV briefed out to all operatives involved in the task.	1
• Industrial disease	x		x
• Disability	4	All Operatives exposed to hand-arm vibration (HAV) trained in HAVS awareness.	4
• Reduction in dexterity	=		=
	16	All vibrating tools and equipment used are of a low vibration specification where reasonably practicable. Each operative's exposure to vibration shall not exceed the exposure limit value (ELV) of 5m/s ² A(8) per day. Hand-arm vibration exposure calculator to be used to determine any restrictions that each specific vibrating tool can be used throughout the working day. Should not be carried out during extreme cold or inclement weather. Operatives shall keep hands warm to allow blood flow. Operatives to be rotated to ensure over-exposure to vibration does not occur. Regular job rotation system should be managed. Pre-use check of all tools and equipment undertaken by the user. Vibrating tools and equipment are to be maintained according to the manufacturer's instructions and tested to ensure accurate knowledge of vibration emitted by each piece of equipment. Do NOT grip the tool too hard. Report any ill health to management immediately. This type of activity should be restricted and avoided where possible.	4

3.12 Work from MEWPS, cherry pickers, scissor lift or other mechanical height access equipment

Hazard Description: 3.12.1 Work from MEWPS, cherry pickers, scissor lift or other mechanical height access equipment

Person at risk: Operative performing the work

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	5	All operatives involved with rescue are trained and competent in the use of specialist rescue equipment.	1
• Falls from height	x		x
• Fatality	5		5
• Dropped objects	=	All operatives required to work at height are trained and competent.	=
• Subsidence/collapse	25	All operators hold valid certification for the MEWP and are deemed competent in operation.	5
		Operative to ensure they are competent to erect and use correctly, if not operative must contact a line manager for additional assistance before using the equipment.	
		All operators to remain in the platform basket at all times.	
		All personnel working from MEWP must wear full body harness and short fixed length lanyard attached to the designated anchor point within the basket.	
		Any localised ground features, e.g. trenches, manholes and un-compacted backfill identified and covered where necessary to prevent collapse.	
		Barriers with appropriate signage to be erected around any delivery area to prevent unauthorised access to throughout the activity.	
		Designated parking area for MEWP's to be determined as part of site traffic management plan.	
		Ensure the MEWP cannot be caught, or impact any overhead obstructions.	
		Following the initial inspection, the operator will inspect the access platform every day before use, according to the manufacturer's instructions.	
		Operation of MEWP will be undertaken by a	

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)

Reference: CAD/UR/W/ MAS/CN - 3647

Page: 29 of 41

Date updated: 26 Aug 26

trained and competent person with relevant IPAF Certification for the type of MEWP.

Pedestrian footpaths to be routed around the designated loading/unloading area.

Pedestrians shall wear hi-visibility clothing as standard PPE on site.

MEWP must only be operated on a firm and level surface with sufficient strength to support the MEWP and gradient per the manufacturer's recommendations.

MEWP to be tested for safety every six months per PUWER &/or LOLER regulations, with copies of documentation readily available.

Operative to use MEWP per training and manufacturer instructions.

Operatives shall secure tools at height with retention strap to prevent dropped object.

Rescue plan developed and discussed with all operatives before commencing with the activity.

Safety helmets will be worn at all times when working at height from MEWPs.

The MEWP shall be regularly repositioned to ensure it remains in the optimum position as the task progresses.

Weather conditions continually assessed before commencing with work at height and during the completion of the activity.

The work area should be suitable pre-determined location and separated from pedestrians and operatives with safe access and walkways provided.

Working platform of MEWP fully enclosed with no risk of fall from height during use.

3.13 Cables

Hazard Description: 3.13.1 Cables

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All Operatives will wear protective footwear with non-slip soles and proper ankle protection at all times.	1
• Slips, Trips and Falls related injuries	x		x
• Bruising	4	Cables to be routed above head height wherever possible.	4
• Cuts	=		=
• Dropped objects	16	Manage all cables and equipment, so they do not cause trip hazards in the working area. Unavoidable trailing cables to be identified and made visible to other persons within the area.	4

3.14 Slippery substances

Hazard Description: 3.14.1 Spilled substance

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All fluids to be stored in a designated area away from walkways and thoroughfares.	1
• Slips and Falls	x		x
• Personal Injury	4	All spillages are immediately cleared up, using spill kit where required, post warning signs and leave in place until the area is safe.	4
• Dropped objects	=		=
	16	Barriers with warning signage displayed around the working area to prevent unauthorised access. Manage and remove potential slipping hazards as they arise and notify site management if additional assistance is required. Spillages cleaned as soon as practicable and in accordance with COSHH assessment requirements.	4

3.15 Stairs

Hazard Description: 3.15.1 Presence of stairs

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All staff will wear protective footwear with non-slip soles and proper ankle protection at all times.	1
• Trips and Falls	x		x
• Personal injury	4	Operatives are required to hold handrails/ bannisters when ascending or descending stairs.	4
• Dropped objects	=	Manual handling risk assessment to be undertaken in the event of materials being manually transported up/down stairs.	=
	16	Stair nosings are highlighted to identify changes in levels.	4

3.16 Materials stored at ground level

Hazard Description: 3.16.1 Equipment and materials stored at ground level

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All staff will wear protective footwear with non-slip soles and proper ankle protection at all times.	1
• Slips, Trips and Falls	x		x
• Personal injury	4	Store all equipment and materials in a designated area away from walkways and thoroughfares to prevent trips and falls.	4
• Dropped objects	=		=
• Potential obstruction during an emergency escape	16	Manage and remove potential slip & trip hazards as they arise and notify site management if additional assistance is required.	4

3.17 Ground level obstacles

Hazard Description: 3.17.1 Ground level obstacles

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All ground level obstacles shall be removed where practicable or identified using hazard warning tape.	1
• Trips and Falls	x		x
• Personal Injury	4	All staff will wear protective footwear with non-slip soles and proper ankle protection at all times.	4
• Dropped objects	=	Thoroughfares and general access shall be planned to reduce exposure to ground level obstacles.	=
	16		4

Hazard Description: 3.17.2 General access and egress around the work area or premises

Person at risk: Operative performing the work, Other Site Operatives

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All spillages are immediately cleared up, using spill kit where required, post warning signs and leave in place until the area is safe.	1
• Slips Trips and Falls	x		x
• Bruising	4		4
• Cuts	=	All staff will wear protective footwear with non-slip soles and suitable ankle protection at all times.	=
• Broken Limbs – Caused by items left on the floor	16	Cables to be routed above head height wherever possible.	4
		Equipment is regularly maintained to prevent leaks onto the floor.	
		Identify any unavoidable trailing cables and make visible to other persons within the area.	
		Manage all cables and equipment, so they do not cause trip hazards in the working area.	
		Manage and remove any potential slip & trip hazards as they arise and notify site management if additional assistance is required.	
		Stair nosings are highlighted to identify changes in levels.	

Store all equipment and materials in a designated area away from walkways and thoroughfares.

3.18 Ground conditions (Terrain)

Hazard Description: 3.18.1 Ground conditions (Terrain)

Person at risk: Operative performing the work, Other Site Operatives, Public

Risk	Risk Rating	Control measures	Residual Risk
Risk of:	4	All pedestrian routes to be free from ground level obstacles where possible.	1
• Slips, trips and Falls	x		x
• Sprained ankle	3	The ground shall be constructed of suitable materials and compacted where required.	3
• Joint injury	=	Lighting to be placed to ensure sufficient levels of luminance outwith daylight hours.	=
• Dropped objects	12	Operatives shall wear protective footwear with proper ankle support on site.	3
		Pedestrian routes to be periodically inspected to ensure they remain suitable.	
		Where the gradient of the pedestrian route becomes excessive, temporary steps/staircases installed where required.	

4.0 COSHH Assessment

4.1 Substance details

Substance name: Silica Dust

Manufacturer: Various

Composition: Natural substance found in most rocks, sand and clay and in products such as bricks and concrete.

Reference Number: 00033

Date Created: 09 Jul 21

Date Reviewed: 13 Aug 26

Reviewed By: Calvin Nash

Next Review Date: 07 Feb 27

Date of SDS: 06/2013

SDS Reference: CIS36 (Rev 2)

4.1.1 Hazardous properties of the substance



Serious Health
Hazard

Exposure Limits

Short Term Exposure Limit:

- Short Term Exposure Limit Not Applicable for this substance

Long Term Exposure Limit:

- Respirable silica 0.1mg/m3

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)

Reference: CAD/UR/W/ MAS/CN - 3647

Page: 35 of 41

Date updated: 26 Aug 26

4.1.2 Activity Details

4.1.2.1

Activity:	Indirect exposure
Details on how the substance is being used:	Dust from drilling activities
Form of Substance:	Dust
Exposure route:	Inhalation
Location:	In a confined Space
Duration of Exposure:	Between 31 minutes and 2 hours
Amount of substance being used:	8hr Working shift
Frequency of use:	Daily
Number of Persons exposed:	Between 2 and 5
Is the material being used outside of its recommended temperature limits?	No
Susceptible persons:	None, Drillers to wear FFP3 masks
Are any other Persons at risk from indirect exposure:	Yes , anyone who has come in contact with the silica
Health surveillance provided:	Respiratory assessment

4.1.2.2

Activity:	Indirect exposure
Details on how the substance is being used:	Dust being created through drilling activities
Form of Substance:	Dust
Exposure route:	Inhalation
Location:	In a confined Space
Duration of Exposure:	Between 31 minutes and 2 hours
Amount of substance being used:	N/A
Frequency of use:	Daily
Number of Persons exposed:	Between 2 and 5
Is the material being used outside of its recommended temperature limits?	No
Susceptible persons:	None
Are any other Persons at risk from Indirect exposure:	Yes , All operatives to wear FFP3 masks
Health surveillance provided:	N/A

4.1.3 Control Measures

Control measure details:	Engineering controls:
Water suppression to keep dust becoming airborne.	Forced ventilation
FFP3 Masks to be worn.	Extraction Unit
	H Class on tool extraction and/or water suppression to be used

PPE Requirements



Head protection



Ear Protection



Protective Footwear with ankle support



Eye Protection - Safety Goggles



Protective Gloves



Fire resistant coveralls (one piece)



FFP3 disposable mask or half mask with P3 filter

Handling and storage details

Handling

- Wear appropriate PPE.
- Use H grade vacuum to clean.
- Dampen collected dust to prevent spread.

Transportation Information

- Not classified as dangerous for transport.

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Holes)

Reference: CAD/UR/W/ MAS/ICN - 3647

Page: 38 of 41

Date updated: 26 Aug 20

4.1.4 Emergency Response

First Aid measures:

Inhalation



- Remove to fresh air.
- Get immediate medical attention after significant exposure or if feeling unwell.

Ingestion



- Do not induce vomiting.
- Wash out mouth with water.

Skin Contact



- Wash with soap/ cleanser and rinse with water.
- If irritation persists then consult a doctor.

Eye Contact



- Irrigate with water until irritation subsides.
- If irritation persists then consult a doctor.

Firefighting measures:

Suitable extinguishing Media:

- Carbon dioxide
- Powder
- Foam

Accidental release measures:

- Ventilate the area.
- Wear heavy duty impervious gloves
- Wear eye protection if contact likely
- Suitable respiratory protection must be worn
- Wear protective overalls and footwear for large spillages
- Scoop or scrape up and place in suitable container

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corre Hoies)

Reference: CAD/UR/W/ MAS/EN - 3647

Page: 39 of 41

Date updated: 26 Aug 26

4.1.5 Disposal

Disposal considerations:

- Dispose or recycle of spillages in a controlled manner

Unit 2, CA Business Park, Colewood Road
Whitstable, CT5 2RP

Website <https://www.cadrillers.com>



By signing below, you are confirming that you are fully aware of the risk assessment findings, the method that the work will be undertaken and the required standard of behaviour at all times while representing the company on site during this project.

[illegible]

Project Name: RAMS - Uplands Retail Ltd - Waitrose - Newport (Corra Holes)
Reference: CAD/UR/W/ MAS/CN - 3647

Page: 41 of 41
Date updated: 26 Aug 25

